

Tilden Ave, S. Bridge St and Cochran


Munson Earthmoving

5/14/2026

Project start date: 5/26/2026

0

Milestone description	2	Assigned to	Progress	Start	Days
Tilden Ave.					
Mobilization/Project Sign		MEMC		5/26/2026	2
Layout/PDF/Erosion Control/Signs		MEMC		5/26/2026	2
Project Test Pits		MEMC		5/28/2026	7
Tilden Ave. 8" Main		MEMC		6/3/2026	21
Tilden Services and Hydrants		MEMC2		6/10/2026	15
Connection at Millet St		MEMC		6/24/2026	1
Pressure Testing and Chlorinate		MEMC		6/25/2026	2
Service Connections/Restore		MEMC2		6/29/2026	8
Baker St and Jericho Rd Connections		MEMC		7/7/2026	2
Prep and Trench Pave		MEMC2-ST Paving		7/9/2026	8
S. Bridge St					
Mobilization/Saw Cutting				6/22/2026	1
12" Tapping Sleeve and Valve				6/25/2026	1
12" Water Main				6/25/2026	15
Service and Hydrants		MEMC2		7/13/2026	10
Pressure Testing and Chlorinate				7/23/2026	2
Service Connections/Restore				7/27/2026	3
Cochran Road East					
Mobilization/Saw Cutting				6/12/2026	1
8" Water Main				6/15/2026	5
Service and Hydrants				7/6/2026	5
Main Line Connection/Testing				7/13/2026	3
Service Connections/Restore				7/16/2026	5
Cochran Road West					
Mobilization/Saw Cutting				6/15/2026	1
8" Water Main				6/22/2026	35
Services and Hydrants				7/20/2026	12
Bridge/Cochran Intersection Connections				8/3/2026	3
Testing, Service Connections				8/10/2026	10
Site Restorations, Concrete Sidewalks				8/8/2026	10
Huntington Road					
Mobilize, Saw Cutting				8/14/2026	1
8" Main Line				8/17/2026	5
Services and Hydrants				8/24/2026	4
Pressure Testing and Chlorinate				8/28/2026	5
Service Connections				9/2/2026	2
Site Restoration, Site Concrete, Asphalt				9/4/2026	8

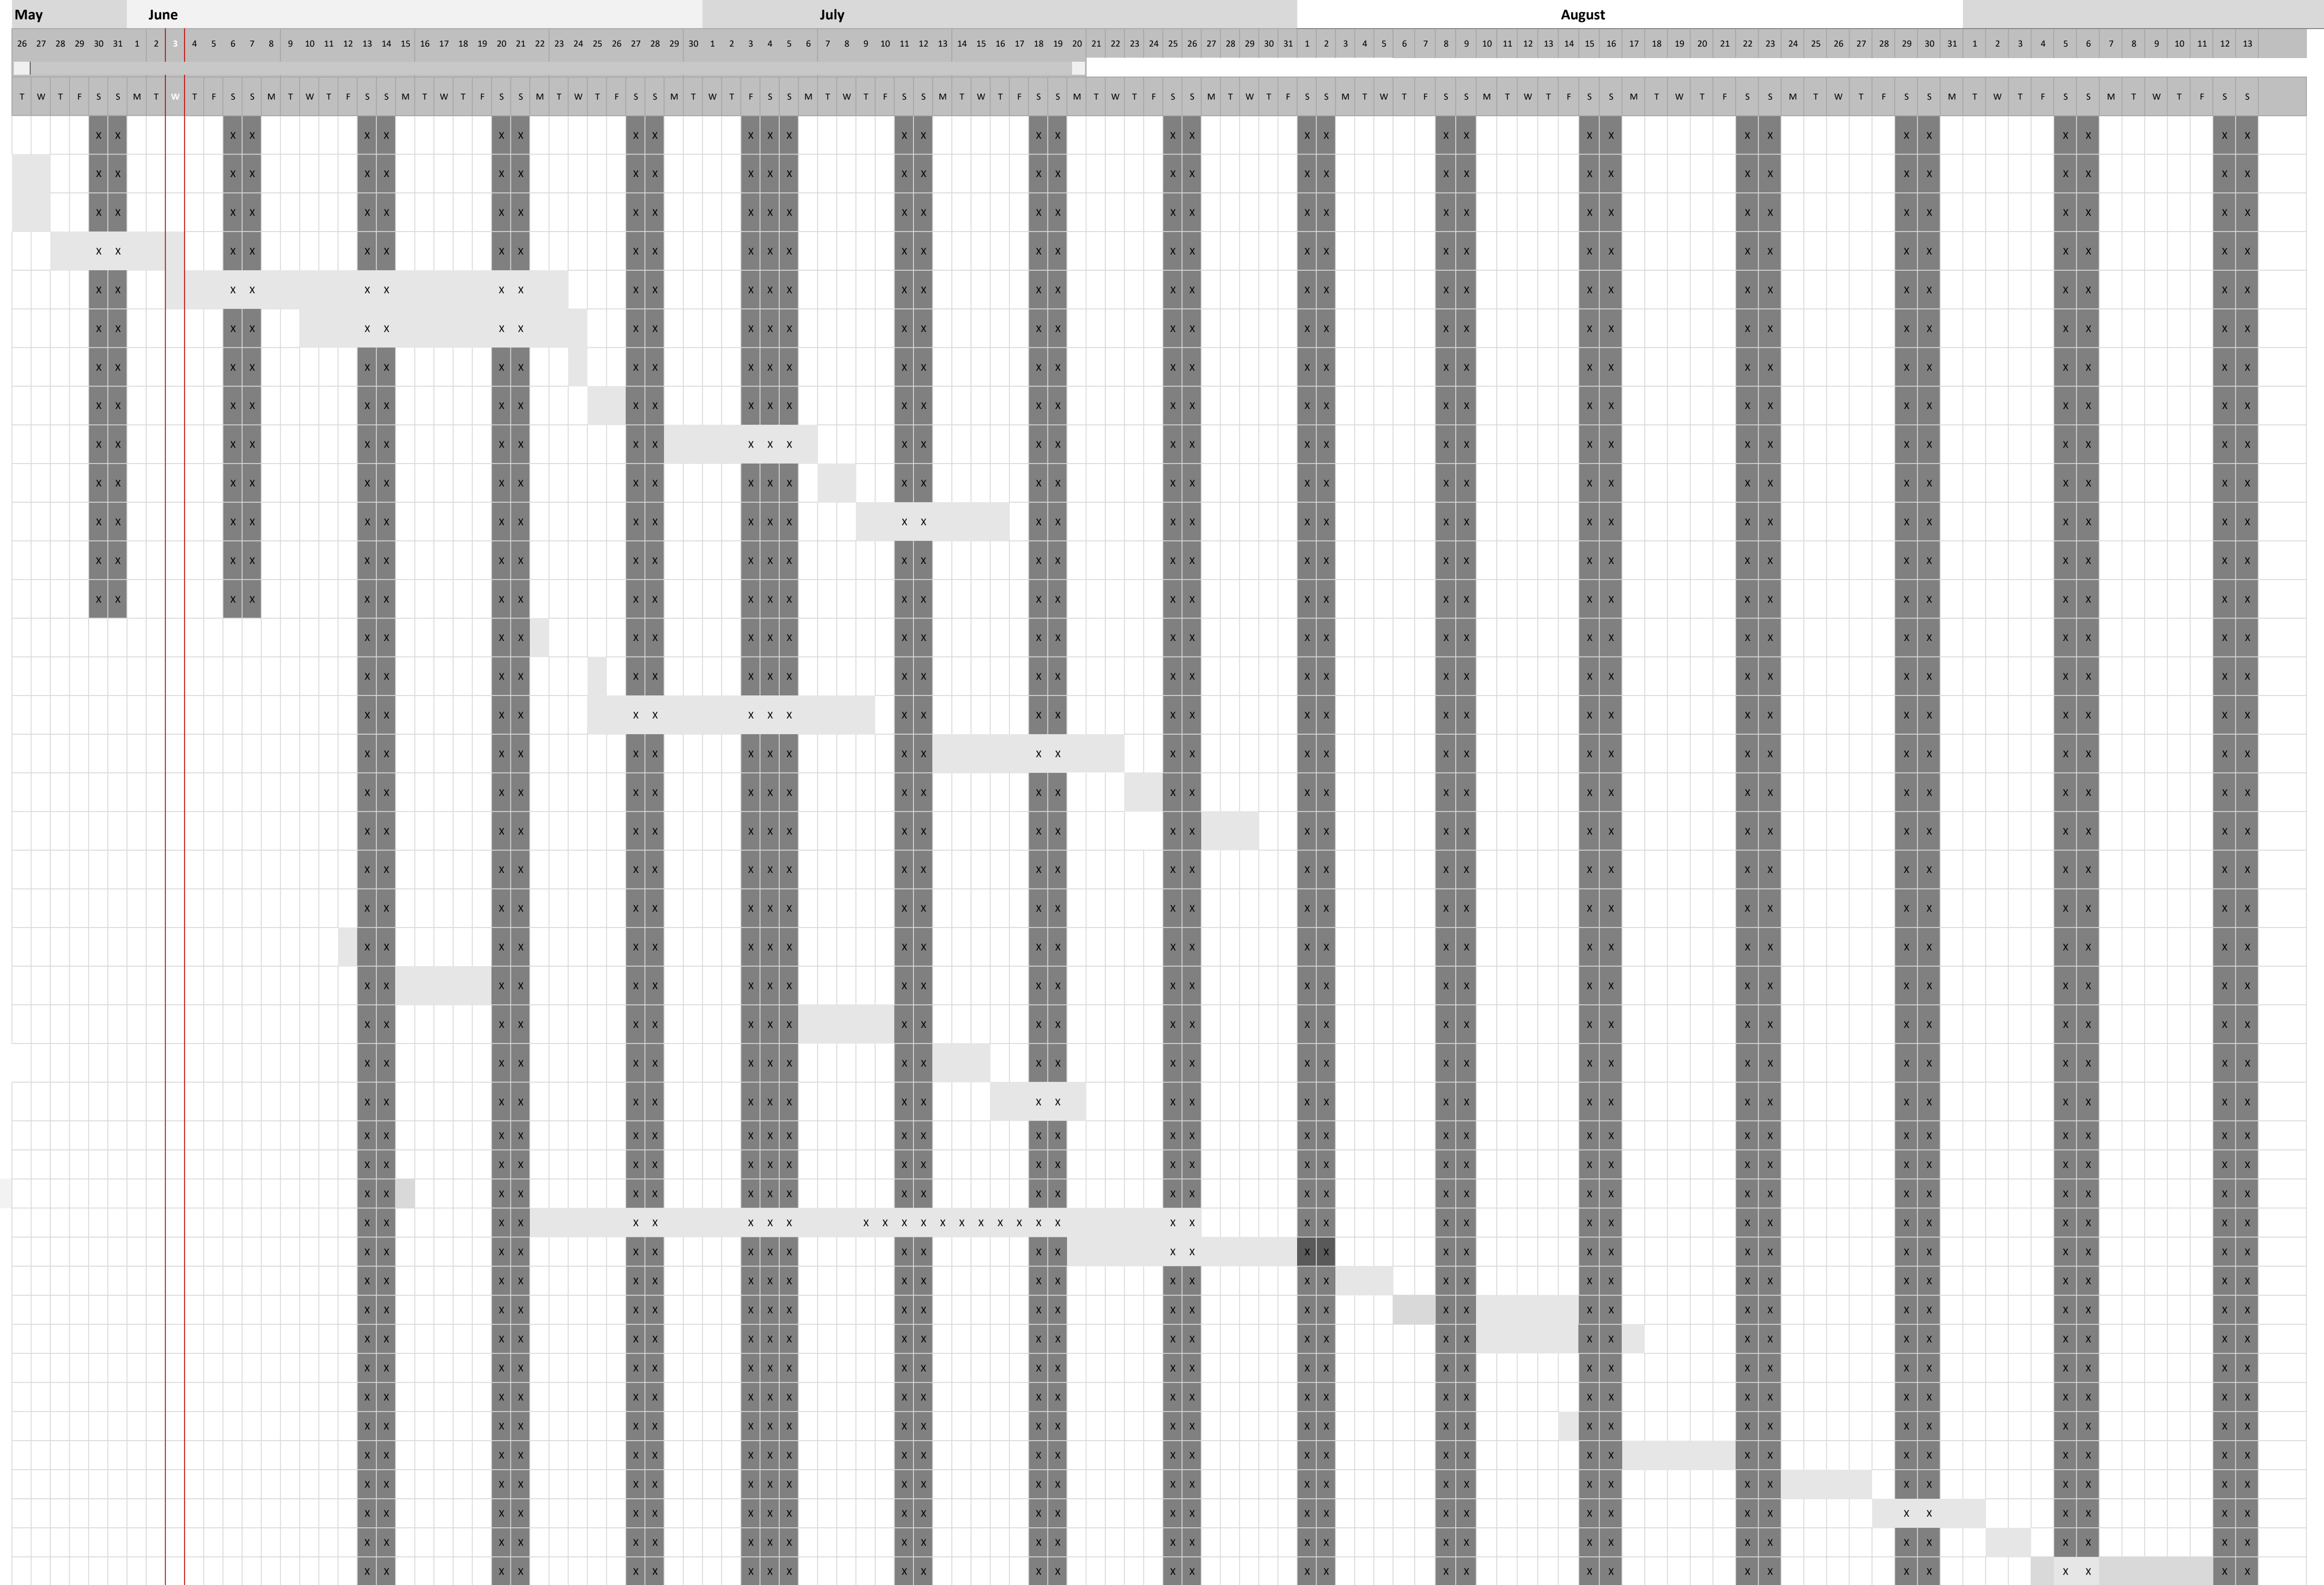

To add more data, insert new rows ABOVE this one

